

	<b>ICS Weekly Project Report</b> November 13, 2020
	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

## High School

- Ⓡ Completed week ending Friday, November 13, 2020
  - Boiler Room
    - Insulation of piping
  - Area C 3<sup>rd</sup> level science rooms
    - Final cleaned and ready for turnover
  - Area C 3<sup>rd</sup> level restrooms
    - Final cleaned and ready for turnover
  - New Athletic Corridor/Elevator
    - Elevator phone hook up
    - Fin tube radiation installation
  - Main Gym
    - Installed volleyball sleeves for auxiliary courts

- Ⓡ Planned week ending Friday, November 20, 2020
  - Boiler Room
    - Commissioning, testing and balancing
  - Area P Link
    - Waiting for windows and storefront door delivery
  - Lower Level Area F Dance Studio/Weight Room/Wrestling
    - Interior glass installation, and waiting for wall pad delivery
  - New Athletic Corridor/Elevator
    - Elevator inspection and turnover

## Centennial Elementary

- Ⓡ Completed week ending Friday, November 13, 2020
  - Contractors continued working to address punch list and IEA Commissioning log items.
  - IEA Commissioning to continue commissioning of the mechanical/HVAC systems.

	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Ⓡ Planned week ending Friday, November 20, 2020

- Contractors to continue working to address punch list and IEA Commissioning log items.
- IEA Commissioning to continue commissioning the mechanical/HVAC systems.

### Sheridan Hills Elementary

Ⓡ Completed week ending Friday, November 13, 2020

- Contractors continued working to address punch list and IEA Commissioning log items.
- IEA Commissioning continued the commissioning of the mechanical/HVAC systems.
- Continued chiller system piping installation in the Lower Level mechanical spaces.
- Started above grade CMU walls on the Kitchen/Receiving area addition.

Ⓡ Planned week ending Friday, November 20, 2020

- Contractors to continue to address punch list and IEA Commissioning log items.
- IEA Commissioning to continue commissioning the mechanical/HVAC systems.
- Complete above grade CMU at the chiller enclosure.
- Continue Lower Level mechanical piping and boiler installation.

### Middle School

Ⓡ Completed week ending Friday, November 13, 2020

- Phase 2 Area D Special Education/Link
  - Installed acoustical ceiling pads throughout
- Phase 2 New Conference Room and Staff Lounge
  - Installed acoustical ceiling pads
- Phase 2 FACS Lab
  - Tape, mud, and sand walls
  - Painted walls
- Phase 2 Chiller Tower
  - Chiller piping continued
- Phase 3 Third Floor Restrooms

	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Installed gyp board ceiling in north restrooms
- Installed toilet partitions in north restrooms
- Started tiling in south restrooms

Ⓡ Planned week ending Friday, November 20, 2020

- Phase 2 Area D Special Education/Link
  - Restroom partitions and toilet accessory installation
  - Wall covering in classrooms
- Phase 2 New Conference Room and Staff Lounge
  - Waiting for casework delivery
- Phase 2 FACS Lab
  - Install ceiling grid
- Phase 2 Chiller Tower
  - Continue chiller piping
- Phase 3 Third Floor Restrooms
  - Install grab bars and accessories in north restrooms
  - Finish tiling in south restrooms

## STEM

Ⓡ Completed week ending Friday, November 13, 2020

- Continued testing, balancing, and commissioning of mechanical systems

Ⓡ Planned week ending Friday, November 20, 2020

- Continue testing, balancing, and commissioning of mechanical systems

## Dual Language

Ⓡ Completed week ending Friday, November 13, 2020

- Contractors continued working to address items noted on the commissioning corrective action log.
- Contractors worked to address issues identified during the 11-month warranty walkthrough.

Ⓡ Planned week ending Friday, November 20, 2020

- Contractors to continue working to address items noted on the commissioning corrective action log.

	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

- Contractors to continue working to address issues identified during the 11-month warranty walkthrough.

	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423


CURRENT PROJECT PHOTOS  
High School – Third Level Restrooms Final Cleaned



High School – Science Classrooms Final Cleaned



High School – Main gym volleyball sleeve installation and athletic corridor fin tube installation

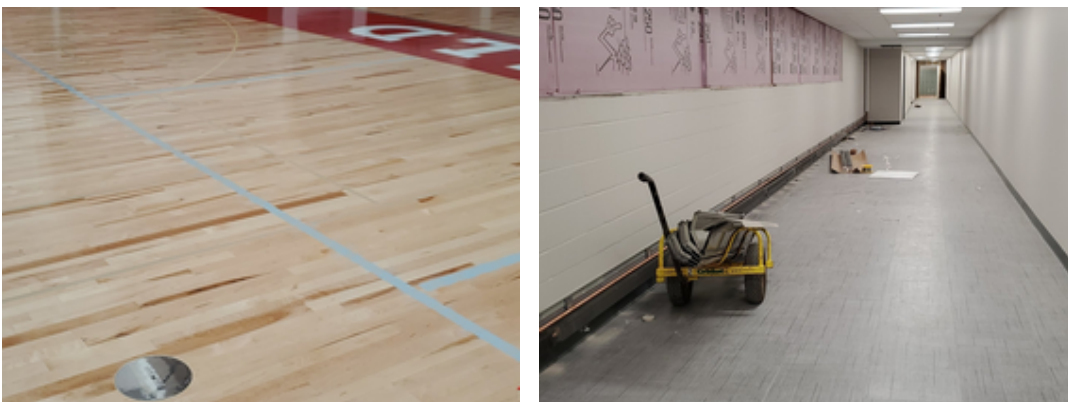



	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Sheridan Hills – Above grade CMU wall progress on the Kitchen/Receiving addition.



Sheridan Hills – Lower Level Mechanical Room progress.




Middle School – Mechanical Equipment - Chiller Piping



	<b>ICS Weekly Project Report</b> November 13, 2020
 <b>RICHFIELD</b> <b>PUBLIC SCHOOLS</b>	ISD #280 Richfield Public Schools 7001 Harriet Avenue S., Richfield, MN 55423

Middle School – Area D Link Restrooms-Sinks and Plumbing Fixtures Installed

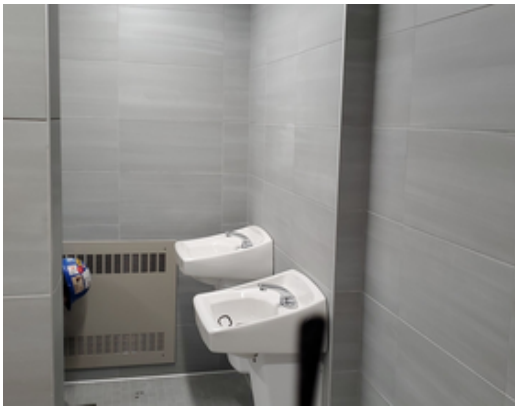

Middle School – Second Level New FACS Lab Drywall Installation and Painted



Middle School – Third Level Restroom Tile and Plumbing Fixtures Installation

